

VAN NESS

IMPROVEMENT PROJECT



Van Ness BAC
October 21, 2021



Agenda

1. Call to Order.
2. Public comment: Members of the public may address the Van Ness Business Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.
3. Approval of Minutes – [April 15, 2021](#)
4. Presentation, discussion and possible action regarding update from SFMTA staff.
 - Project schedule.
 - Construction update.
 - Business support.
 - Outreach update.
 - Update on neighboring projects.
5. Adjourn.

BAC administration reminder

- BAC members are asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

Public Comment


- See Public Comment Policy on back of agenda.
- Public comment for matters that are within the Van Ness Business Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes

April 15, 2021

Staff updates

- Project schedule

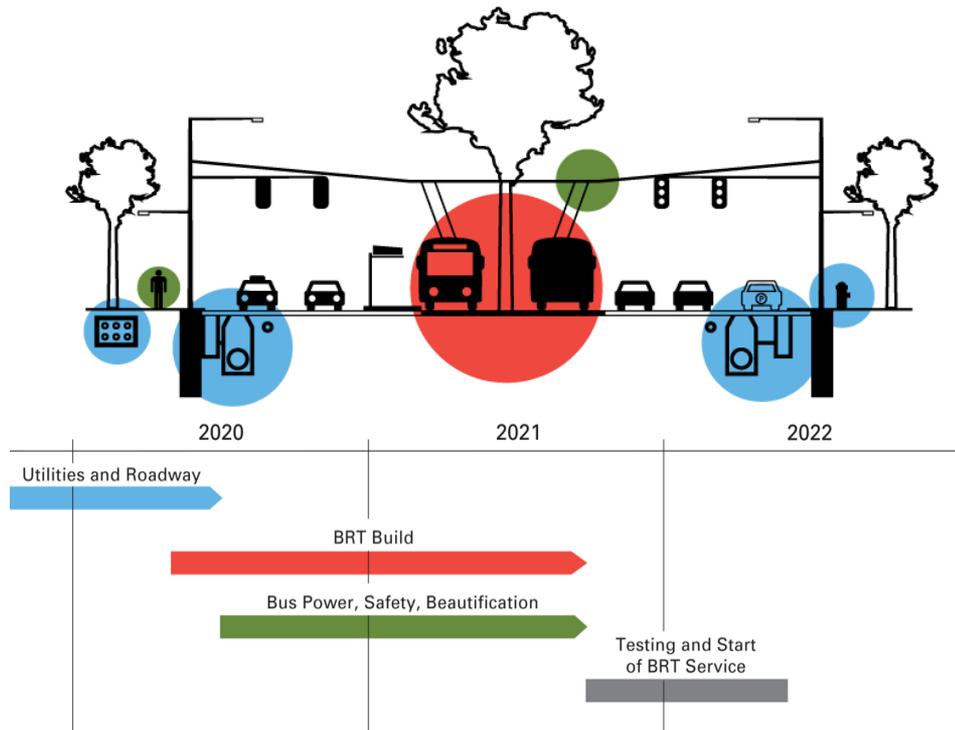

Start	Finish
Fall 2016	Winter 2022
Summer 2020	Fall 2021
Spring 2021	Summer 2021 to Fall 2021

Staff Updates

Contract Modification #14

- Adjustments to light/Muni poles and foundations
- Revise irrigation systems
- Additional traction power cable
- Furnish and install CCTV poles and foundations
- Repair work to existing roadway

Total is \$717,878, to be funded through existing project budget.
This does not extend the length of the project.

Staff Updates

Construction update

Current work

- ~95% of the bulb out work is complete
- Irrigation and backfill work ongoing in the median
- All traffic signals except Lombard have been cutover to the new signal boxes
- Tree planting at the sidewalk is progressing towards Mission; median trees to follow

Staff Updates

Outreach Updates

- Fall 2021 quarterly newsletter forthcoming
- Currently planning for opening ceremony early Spring 2022

Staff Updates

Geary Rapid Project

Construction work on the [Geary Rapid Project](#), in coordination with San Francisco Public Utilities Commission and San Francisco Public Works, is nearly complete. Installation of red transit lane treatments is underway. All other contract work is complete, including 1.5 miles of new sewer, almost three miles of upgraded water mains, 1.5 miles of roadway repaving, three new and eight upgraded traffic signals, four new pedestrian crossings, 32 pedestrian bulb-outs, 12 transit bulb-outs and 38 upgraded curb ramps.

Questions or concerns? Contact GearyRapid@SFMTA.com or 415.646.2300.

For more information visit SFMTA.com/Geary or contact GearyRapid@SFMTA.com

Next Meeting



February 17, 1:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

SFMTA.com/VanNess

