

VAN NESS

IMPROVEMENT PROJECT



Van Ness BAC
June 17, 2021



Agenda

1. Call to Order.
2. Public comment: Members of the public may address the Van Ness Business Advisory Committee on matters that are within its jurisdiction and are not on today's calendar.
3. Approval of Minutes – [April 15, 2021](#)
4. Presentation, discussion and possible action regarding update from SFMTA staff.
 - Project schedule.
 - Construction update.
 - Business support.
 - Outreach update.
 - Update on neighboring projects.
5. Adjourn.

BAC administration reminder

- BAC members are asked to RSVP to confirm quorum.
- If no quorum can be reached, meeting to be canceled.

Public Comment


- See Public Comment Policy on back of agenda.
- Public comment for matters that are within the Van Ness Business Advisory Committee jurisdiction and are not on today's calendar.

Approval of Minutes

April 15, 2021



Staff updates

- Project schedule


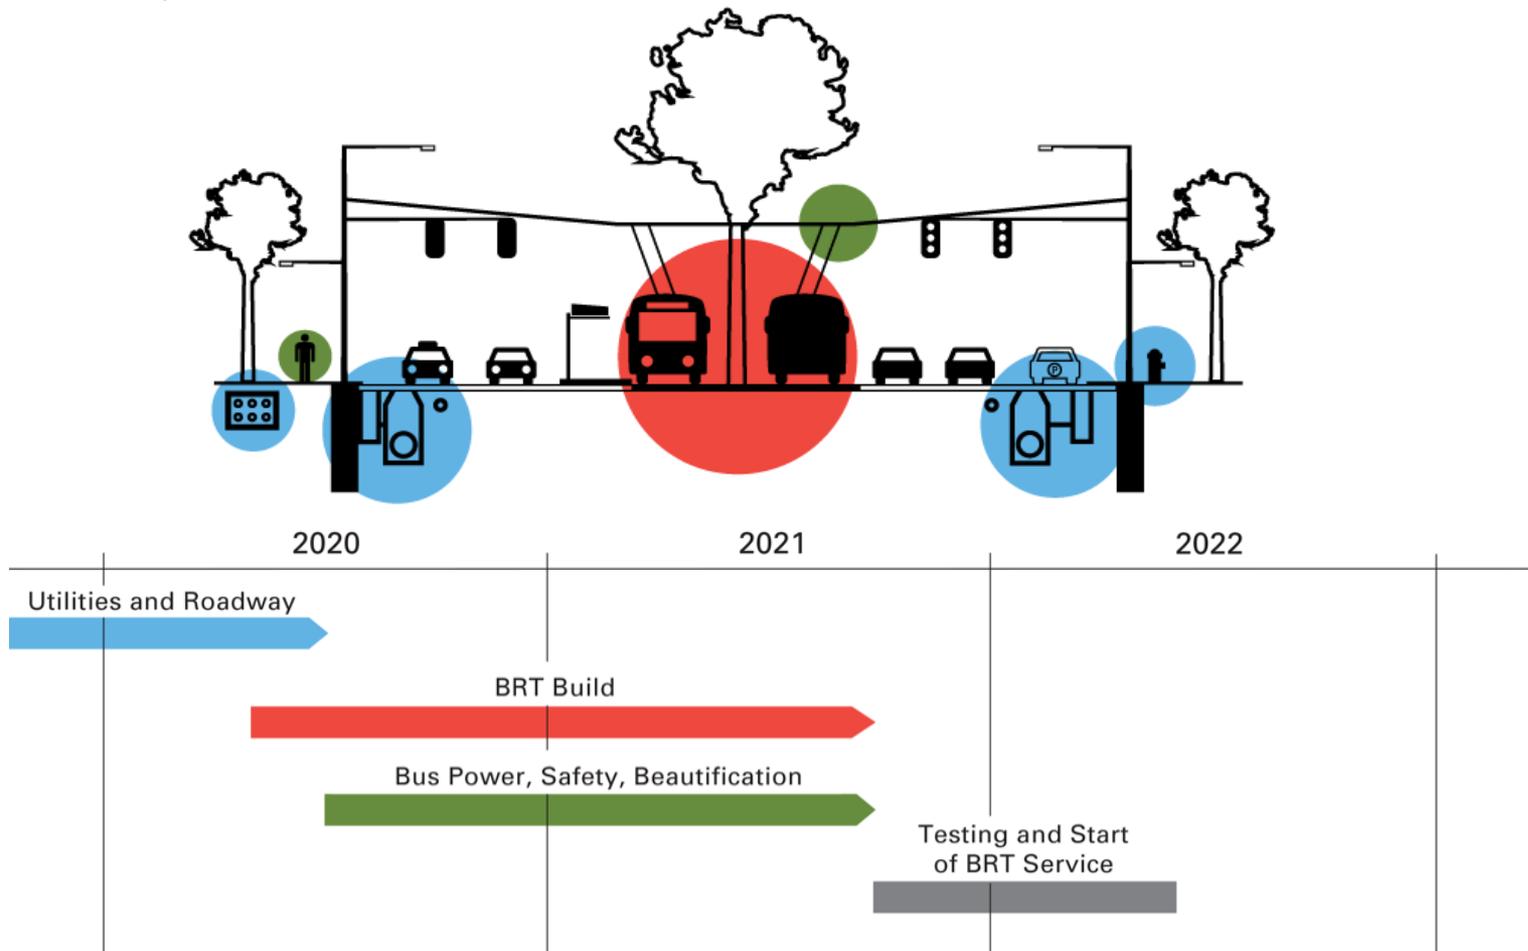


Project Schedule

- Phases 1A and 1B almost complete.



- Phases 1C and 1D almost complete.






	Start	Finish
1A	Fall 2016	Spring 2021*
1B	Summer 2018	Spring 2021*
1C	Summer 2019	Spring 2021*
1D	Fall 2019	Spring 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Spring 2021 to fall 2021

*Estimated

Project schedule as of May 7, 2021

Project Schedule

- Phase 2 in progress.



- Phase 3 in progress.



	Start	Finish
1A	Fall 2016	Spring 2021*
1B	Summer 2018	Spring 2021*
1C	Summer 2019	Spring 2021*
1D	Fall 2019	Spring 2021*
2	Summer 2020*	Fall 2021*
3	Spring 2021*	Spring 2021 to fall 2021

*Estimated

Project schedule as of May 7, 2021

Staff Updates

Construction update

- BRT Buildout Phase in progress
 - Construction of red transit lanes, median islands, bus shelters, bulb-outs, overhead lines, trees
- Likely weekend closure of Mission St. and Market St. intersections in August



Staff Updates

Business support

- City and state reopened June 15
- SF New Deal is providing grants of \$2,500 each to 400 small businesses in San Francisco
 - Eligibility info is available at SFNewDeal.org
 - Deadline is June 30

Staff Updates

Outreach Updates

- Recent activities:
 - Quarterly spring newsletter was sent by mail
- Upcoming outreach activities:
 - Quarterly summer newsletter to be sent by email
 - Planning underway for public celebrations at the end of the project
 - Intersection shut down outreach

Staff Updates

Geary Rapid Project

As part of the [Geary Rapid Project](#), work involves replacing aging water infrastructure in continued coordination with San Francisco Public Utilities Commission. Surface transportation improvements are also underway and being managed by San Francisco Public Works, including traffic signals and streetlights, sidewalk extensions at bus stops and intersection corners, improving median refuges and restriping the newly paved roadway.

For more information visit [SFMTA.com/Geary](https://www.sfmta.com/Geary) or contact GearyRapid@SFMTA.com

Neighboring Project Updates

Caltrans Lombard Street Daytime Lane Closures

Following the [Lombard Vision Zero Project](#), Caltrans recently completed roadway improvements on the US 101/Richardson-Lombard corridor between Francisco Street and Van Ness Avenue. This included repaving the roadway, restriping the lanes and crosswalk and upgrading curb ramps. The SFMTA Board of Directors recently approved High Occupancy Vehicle (HOV) lanes to be added on the corridor. MTA is working with Caltrans to obtain a permit to implement the HOV lanes.

For real-time information, please visit Caltrans QuickMap: quickmap.dot.ca.gov

Next Meeting



October 21 1:00 p.m.

Thank You



VAN NESS

IMPROVEMENT
PROJECT

SFMTA.com/VanNess

